


La Canada Pipeline Project

Spring 2026




Project Overview

Replacing 3,860 linear feet of existing 8" watermain

- Located on La Canada Rd between Hillrise & Via Monserate
- Focused on upgrading infrastructure due to frequent leaks and aging infrastructure
- **Goal:** Improve reliability and sustain water quality in the area



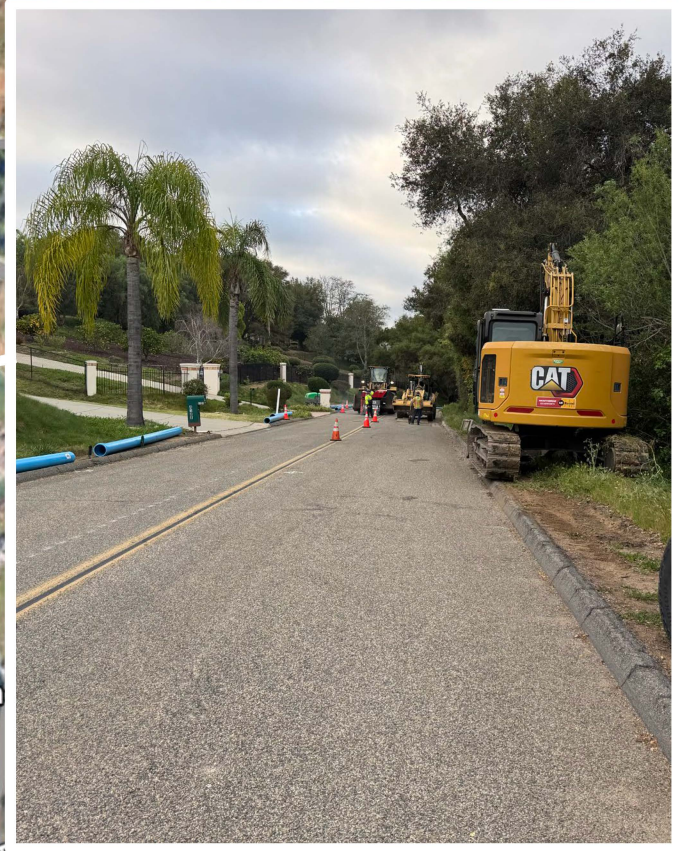



EFI-SOLUTIONS
efi-solutions.com


MURRIETA DEVELOPMENT CO
C/O JOBSITE
BONSALL, CA

94535-01



WARNING
TOXIC FUMES WILL BE EMITTED
AND/OR EXPLOSION
NEVER
OXYGEN ENRICHED ATMOSPHERE
OR FLAMMABLE



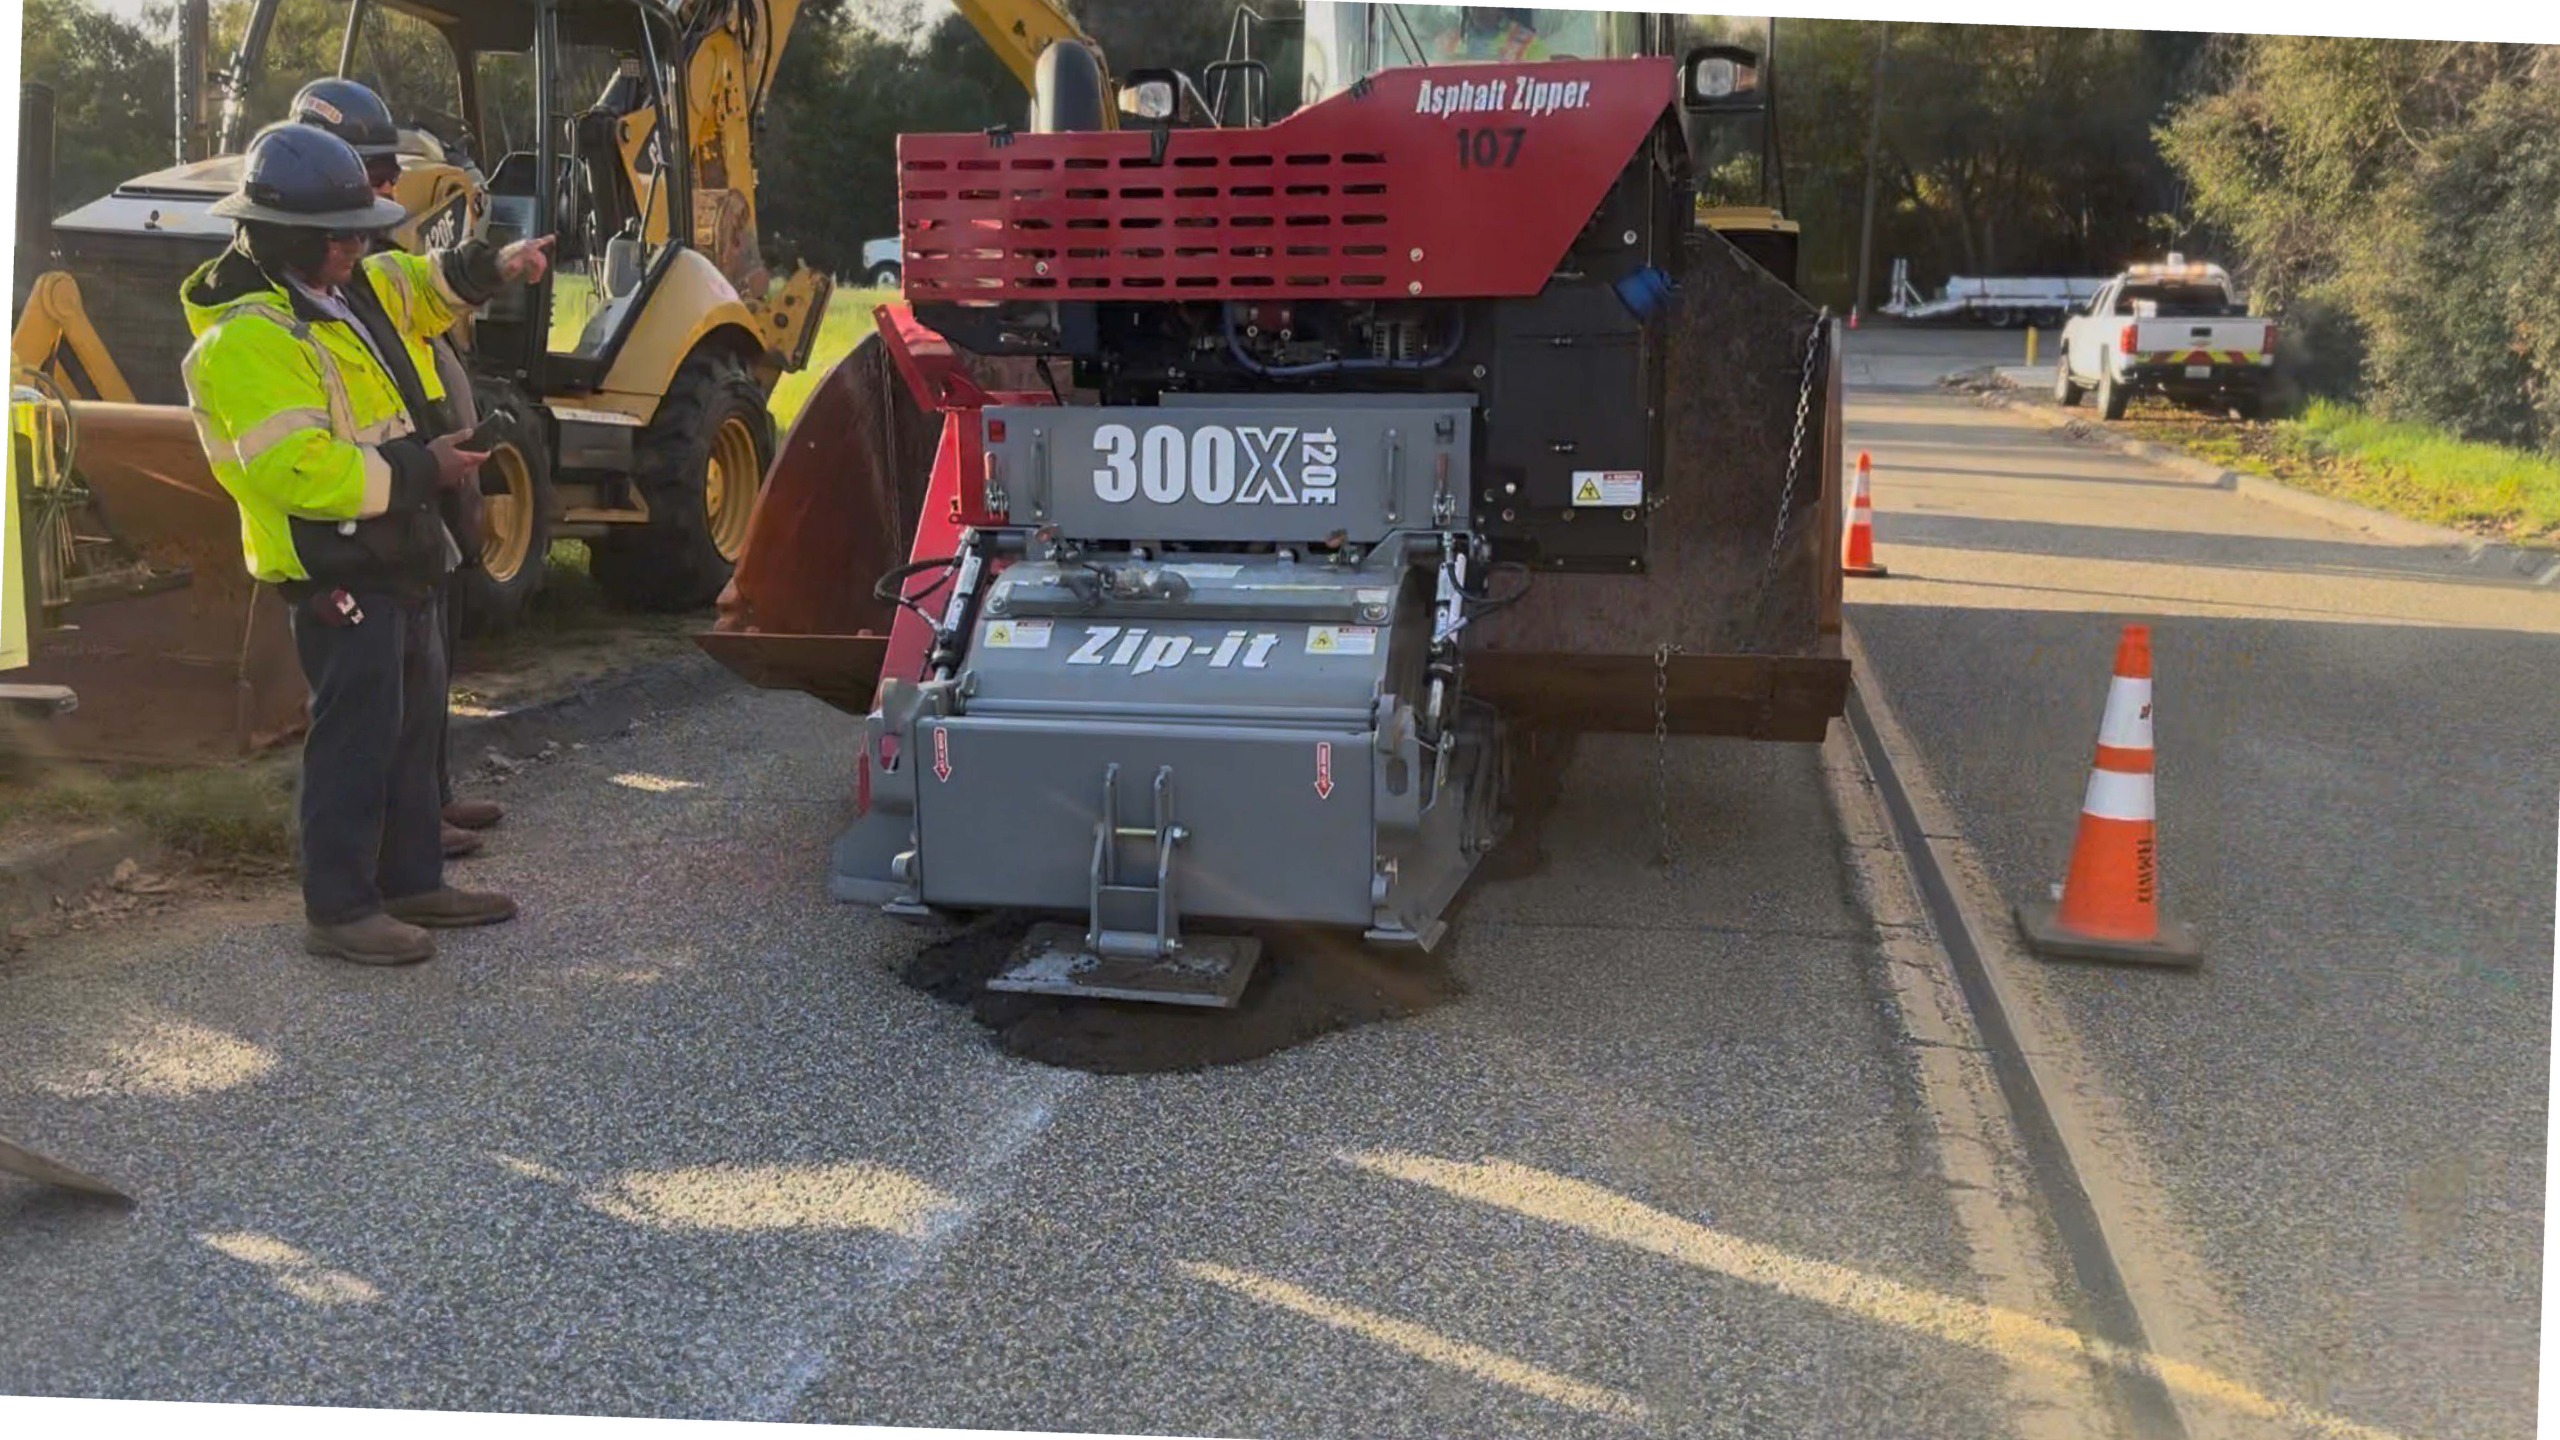



Construction Activities

Days

31

- Pressure Reducing Stations Installation



7

- Potholing



19

- Pipe Installation



8

- Services, Hydrant Installation



4

- Pipeline Tie-ins



5

10

15

20

25

30


69 Total Days








Change Orders




Weather delays

- One week of rain



Ground Water




Thickness of pavement







Keys Take Aways




Staffing: 8-10 crew members/day



Leaks: While laying pipe slowed down progress



Pipe Laid: 200-300 feet/day



Customer Outreach: Calls, door knocking, letters, newsletter, and website





Questions

